

Weekly onshore construction status report

Week of April 07, 2025:

Completed Activities

The contractor activities included:

Cable Route

Horseblock Road (CR 16) and Manor Road

- Began to remove temporary access road
- Placed topsoil and seed

William Floyd Parkway (CR 46) ([Detour for Westminster and Argyle Drive and Extended Hours](#))

- Continued trenching and conduit installation activities
- Continue vault installation activities
- Continue dewatering activities

PSEG-LI right of way (Weekend work)

- Continued trenchless crossing activities
- Continued trenching and conduit installation activities

Revilo Avenue ([Access to the S. Service Road of Sunrise Highway is closed](#))

- Continued mobilization of equipment
- Continued site prep for trenchless crossing activities

Surrey Circle, Union Avenue, Waverly Avenue and Long Island Avenue

- Continue installation of ADA compliant sidewalk ramps
- Placed topsoil and seed

Union Avenue Onshore Converter Station

- Continued build out interior of buildings and equipment testing
- Continued installation of above and below grade facilities
- Continued erecting steel structures

Holbrook Substation Expansion

- Continued substation civil works
- Continued build out interior of building
- Continued overhead bus work

Weekly onshore construction status report

Smith Point County Park & Marina (Weekend Work & Extended Hours)

- Continued mobilization and demobilization of equipment
- Continued trenching and conduit installation activities
- Continue Intercoastal Horizontal Direction Drilling activities
- Continue pipe stringing activities
- Continued installation of the transition joint bay
- Continued dewatering activities
- Continue installation of sheeting

Week of April 14, 2025:

Upcoming Activities

The contractor intended activities include:

Cable Route

Horseblock Road (CR 16) and Manor Road

- Continue to remove temporary access road
- Continue to place topsoil and seed

William Floyd Parkway (CR-46) ([Detour for Argyle Drive and extended hours](#))

- Continue trenching and conduit installation activities
- Continue dewatering activities

PSEG-LI right of way (Potential weekend work and extended hours)

- Continue trenchless crossing activities
- Continue trenching and conduit installation activities

Revilo Avenue ([Access to the S. Service Road of Sunrise Highway will be closed](#))

- Continue mobilization of equipment
- Continue site prep for trenchless crossing activities
- Continue trenchless crossing activities

Surrey Circle, Union Avenue, Waverly Avenue and Long Island Avenue

- Continue installation of ADA compliant sidewalk ramps
- Continue to place topsoil and seed

Union Avenue Onshore Converter Station

- Continue to build out the interior of buildings and equipment testing
- Continue installation of above and below grade facilities
- Continue to erect steel structures

Weekly onshore construction status report

Holbrook Substation Expansion

- Continue substation civil works
- Continue build out the interior of buildings
- Continue overhead bus work

Smith Point County Park & Marina (Weekend Work & Extended Hours)

- Continue mobilization and demobilization of equipment
- Complete Intercoastal Horizontal Direction Drilling activities
- Continue trenching and conduit installation activities
- Continue installation of transition joint bay
- Continue dewatering activities
- Continue installation of sheeting
- Continue vault installation activities

Week of April 21, 2025:

The contractor intended activities include:

Cable Route

William Floyd Parkway (CR-46)

- Continue trenching and conduit installation activities
- Continue dewatering activities

PSEG-LI right of way

- Continue trenchless crossing activities
- Continue trenching and conduit installation activities

Revilo Avenue ([Access to the S. Service Road of Sunrise Highway will be closed](#))

- Continue mobilization of equipment
- Continue site prep for trenchless crossing activities
- Continue trenchless crossing activities
- Install landscaping

Union Avenue Onshore Converter Station

- Continue build out the interior of buildings and equipment testing
- Continue installation of above and below grade facilities
- Continue to erect steel structures

Holbrook Substation Expansion

- Continue substation civil works

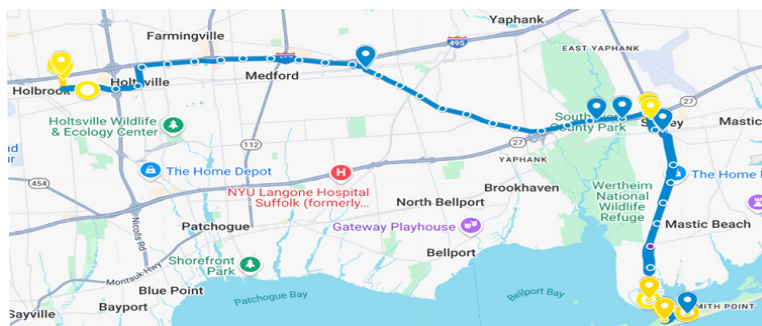
Weekly onshore construction status report

- Continue build out the interior of buildings
- Continue overhead bus work




Smith Point County Park & Marina (Weekend Work & Extended hours)

- Continue mobilization and demobilization of equipment
- Continue trenching and conduit installation activities
- Continue installation of transition joint bay
- Continue dewatering activities
- Continue installation of sheeting
- Continue vault installation activities

Laydown yards will continue to be used for utility, storage, and parking.



[Click here to view the construction progress map.](#)

-  Active construction
-  Temporary restoration
-  Completed restoration

NY State Waters

For the latest information on Sunrise Wind Offshore Activities and to sign up and receive the mariners report please click [here](#).

If you have any questions about any information contained in this notice or any other Project-related matter, please call our hotline at 631-629-8410 or email us at info@sunrisewindny.com.

Best Regards,
The Sunrise Wind Team

Website: www.Sunrisewindny.com

Follow us on X: @Sunrisewindny

Hotline: 631-629-8410

Email: info@sunrisewindny.com
